

CAPEX & WBS Control Hub

Administrator Guide — User Acceptance Testing environment

Environment	UAT on Zoho Catalyst AppSail (India DC), PostgreSQL on Supabase
Address	https://wbs-capex-uat-50045784768.development.catalystappsail.in
Application build	63b07c6 (deployed 14 September 2026), schema 036
Data	Synthetic test data only. ERP connection: Zoho ERP demo tenant 60074128927
Audience	UAT administrators and testers
Version	1.0, 14 September 2026

Every screenshot in this guide was taken from the UAT instance on 14 September 2026 with a synthetic Administrator account. No credential, token or secret appears in this document.

Contents


1. About the application
2. The UAT environment and what the banner means
3. Roles and what each may do
4. Signing in, forgotten passwords, changing a password
5. Finding your way: navigation and the shell
6. Modules and screens
7. How to operate: the core procedures
8. Administrator tasks
9. Exports (CSV and Excel)
10. Notifications
11. Governance: audit trail and controls
12. Zoho ERP integration
13. Frequently asked questions
14. Settings the platform owner controls

1. About the application

The CAPEX & WBS Control Hub is the capital-expenditure control system for projects structured as a Work Breakdown Structure (WBS). It holds the approved budget for every project, WBS element and budget head; checks every purchase request against the money actually available; runs maker-checker approvals; commits purchase orders; reads receipts and vendor bills back from Zoho ERP; reconciles ordered, received and billed values; and carries the project to capitalisation with a complete, tamper-evident audit trail.

What it controls

- **Budget** per control cell (project → WBS element → budget head), with revisions, transfers and version comparison.
- **Exposure** = open PO commitment + actual CWIP (billed) + purchase-request reserves + internal material allocation + internal consumption. Available budget is budget minus exposure. Nothing is approved past what is available without a recorded exception.
- **Maker-checker** on every approval: the person who raised or edited an object may not approve it. An Administrator may override this deliberately, with a reason, and the override is recorded and notified.
- **Money** is always integer paise internally and shown in Indian format (₹, lakh, crore). Foreign-currency orders keep their currency and rate.
- **Audit**: every change is an append-only, hash-chained entry.

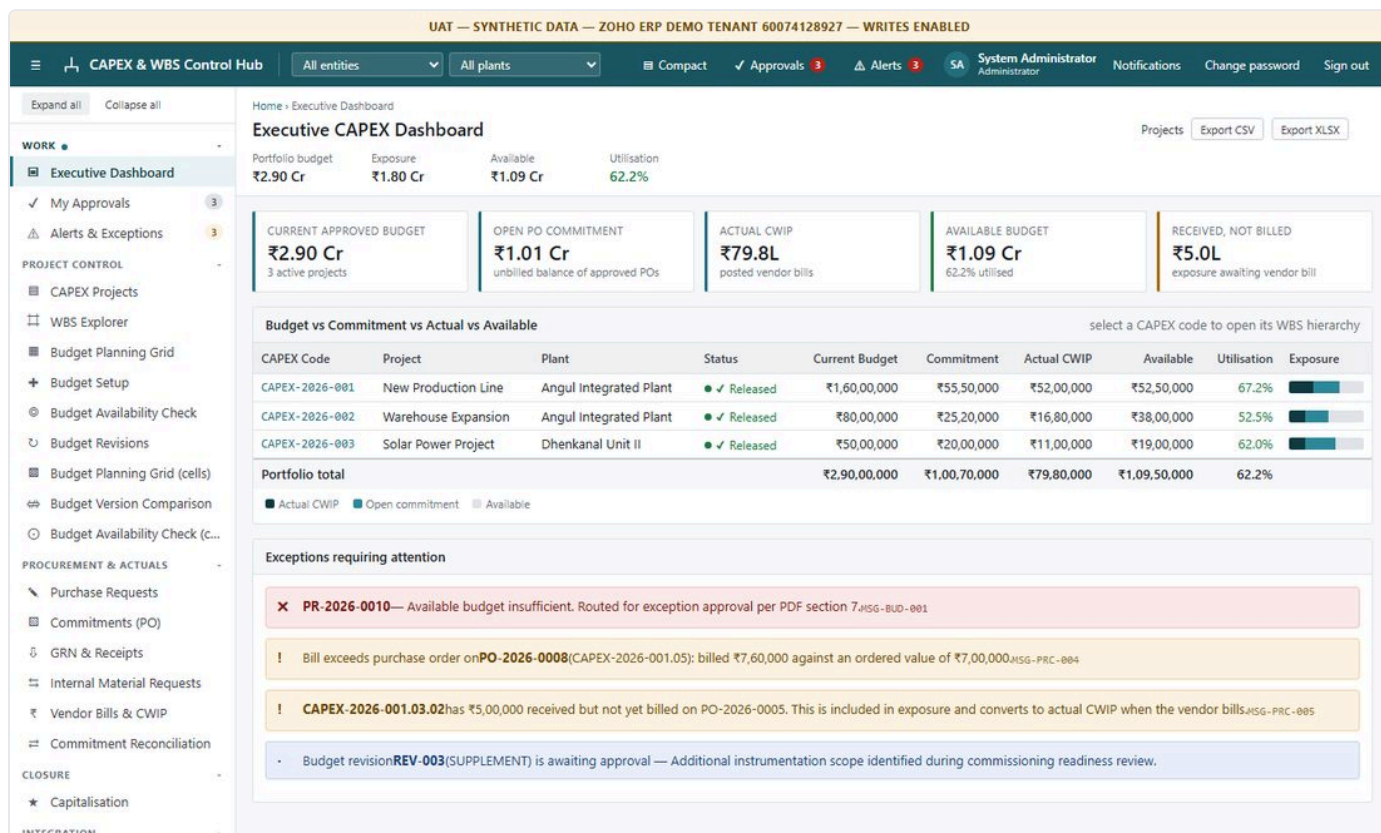

Executive CAPEX Dashboard: portfolio budget, exposure, available, utilisation, and the exceptions needing attention.

2. The UAT environment and what the banner means

The yellow banner at the top of every page reads **UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED**. It means:

- **Synthetic data:** projects, budgets, vendors and documents are test data. Nothing here is a real transaction.
- **Zoho ERP demo tenant:** the connector is bound to one demo organisation only. Purchase orders approved here can be emitted to that tenant; receipts and bills from it are read back.
- **Writes enabled:** outbound purchase-order creation to the demo tenant is switched on under permanent boundaries (one organisation, purchase orders only, every order must be approved here first, identical retries never create duplicates).

What testers must not do: do not treat any figure as real; do not expect e-mail to arrive (mail is recorded, not sent, until the owner verifies a sender); do not share your test password; report anything surprising rather than working around it.

Item	Value
Address	https://wbs-capex-uat-50045784768.development.catalystappsail.in
Health pages	/healthz (process alive), /readyz (database schema ready; expected schema 036), /api/health (application state)
API documentation	Deliberately not published on UAT (/docs answers 404).
Session	Kept in the browser tab only; closing the tab signs you out. Sessions expire; sign in again.

3. Roles and what each may do

Access is by role, enforced on the server for every request. A screen you may not use is not offered in the navigation, and a direct link to it is corrected back to Home. The Administrator holds every permission (a product decision of 13 September 2026), including approvals, but remains subject to maker-checker unless it records a deliberate override (section 8).


Role	Typical person	May
Requestor	Project engineer	Read budgets, run availability checks, raise purchase requests, internal material requests and budget revisions, act on approvals assigned to them, export.
BudgetController	Project controller	Everything a Requestor may, plus budget setup and categories, master data, fulfilment decisions, allocate/issue internal material, period transitions, delegations.
ProcurementApprover	Procurement head	Approve within-budget purchase requests and internal material requests; amend, cancel and close purchase orders; fulfilment decisions.
FinanceApprover	Finance	Approve exception (over-budget) requests and budget revisions, void bills, manage exchange rates, apply period reopenings, allocate capitalisation.
CapitalisationApprover	Fixed-asset accountant	Approve capitalisation; apply period reopenings.
Auditor	Internal audit	Read-only: budgets, the audit trail, the connector and exchange rates. Deliberately no approval inbox: an auditor reads history through the audit trail.
Administrator	UAT administrator	Every permission, plus the notification outbox, identity linking, dispatch, and the recorded self-approval override.

The UAT test accounts cover each role (U-REQ, U-PM, U-PLH, U-PROC, U-FIN, U-PFC, U-CFO, U-AUD, U-ADM) plus four Administrator accounts for the ERP-linked people. Passwords are held by the UAT coordinator and are never written in this guide.


4. Signing in, forgotten passwords, changing a password

Sign in with a WBS account

Open the address, enter your user id and password, and press **Sign in**. Repeated failures are throttled; wait a few minutes and try again.

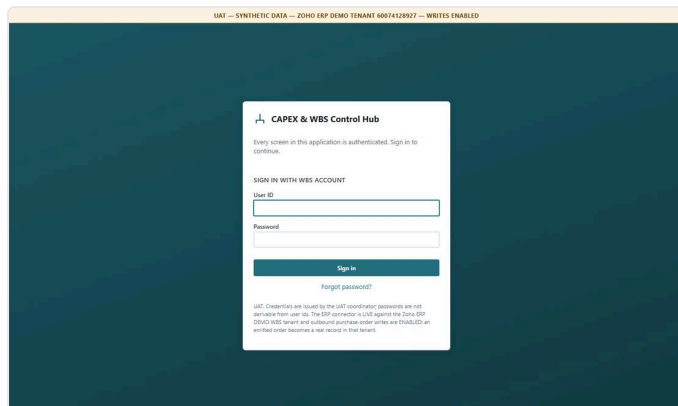

The sign-in page. "Continue with Zoho" appears only once the owner has configured single sign-on (section 14).

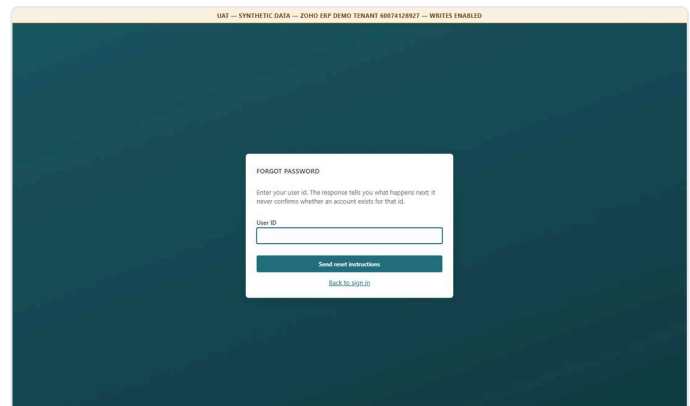

Forgot password: enter the user id; the answer is always the same sentence whether or not the account exists.


Forgot password

1. Click **Forgot password?**, enter your user id, press **Send reset link**.
2. A reset link valid for **15 minutes**, usable **once**, is generated and queued as a notification.
3. On UAT, mail is recorded rather than sent. Ask the Administrator, who can release the link to you from the notification outbox when the owner has enabled that (section 8). Once a real sender is verified, the link arrives by e-mail.
4. Open the link, choose a new password, confirm. Every other session you had is signed out.

Password policy: at least 12 characters with upper case, lower case and a digit; not your user id; not any of your last five passwords; not the seeded starter password.

Change password (signed in)

Use **Change password** in the top bar. You enter the current password and the new one twice. Your current session continues; every other session is signed out.

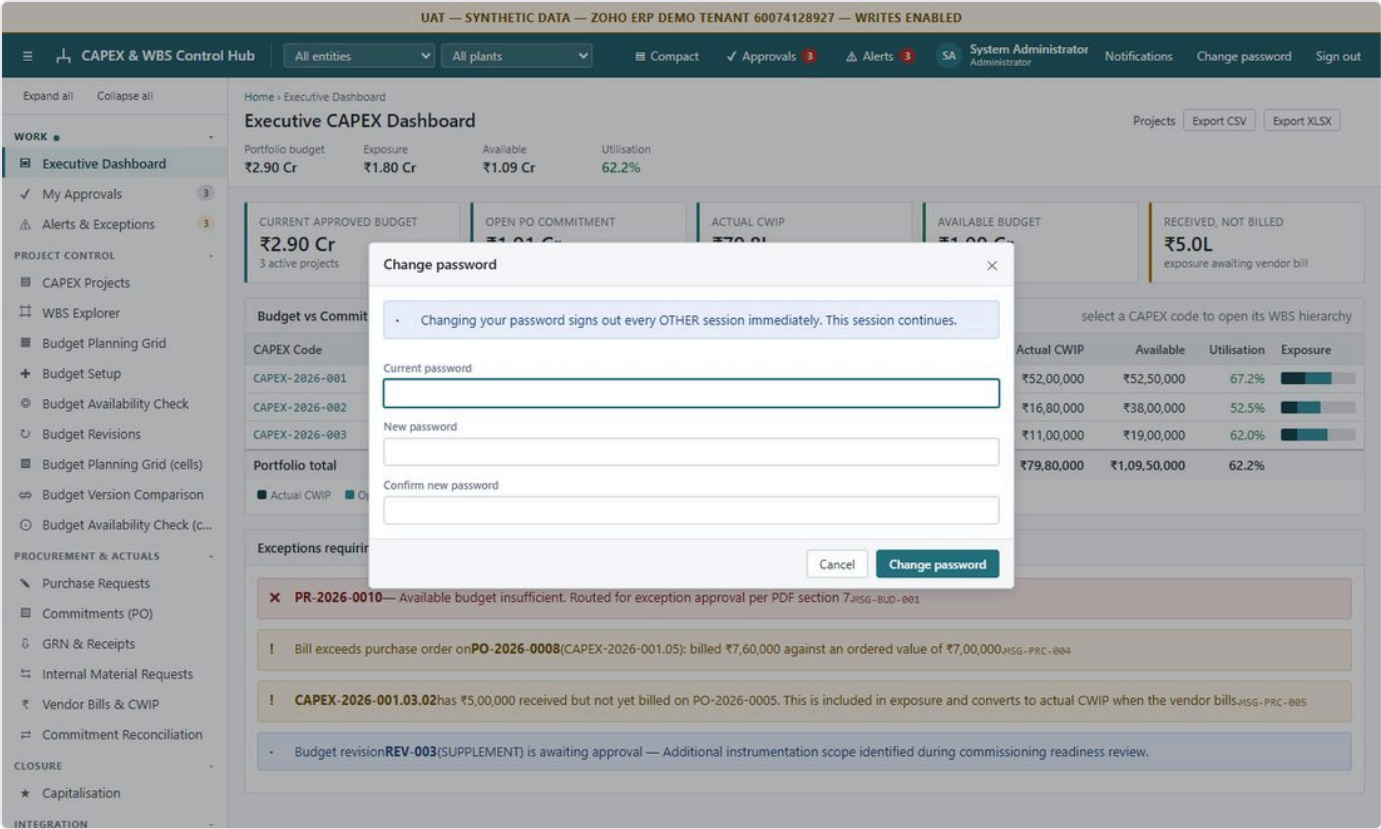

Change password from the identity area.

5. Finding your way: navigation and the shell

- **Left rail:** screens are grouped (Work, Project Control, Procurement & Actuals, Closure, Integration, Governance, Analytics, Integration Mapping). Every group is a collapsible button; **Expand all** / **Collapse all** act on every group. Your choice is remembered per browser tab. The group holding the screen you are on is always opened.
- **Top bar:** entity and plant filters (they scope the registers and the exports), the **Compact** density toggle, badges for **Approvals** and **Alerts** waiting for you, then your name and role, **Notifications** (your preferences and history), **Change password**, **Sign out**.
- **Breadcrumb and page actions:** under the top bar. Create buttons and export controls sit on the right of the page title.
- **Narrow screens:** below 900 px the rail becomes a drawer opened with the ☰ button.
- **Deep links:** every screen has an address (#prs , #imrs , #approval-inbox ...). Back and Forward work as expected.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub | All entities | All plants | Compact | Approvals 3 | Alerts 3 | SA System Administrator Administrator | Notifications | Change password | Sign out

Expand all | Collapse all

Home > CAPEX Projects > CAPEX-2026-001

WBS Hierarchy — New Production Line | Expand all | Collapse all | WBS elements | Export CSV | Export XLSX

CAPEX code: CAPEX-2026-001 | Plant: Angul Integrated Plant | Status: Released | Current budget: ₹1,60,00,000 | Exposure: ₹1,07,50,000 | Available: ₹52,50,000 | Utilisation: 67.2%

Project: CAPEX-2026-001 — New Production Line

Parent rows show the rolled-up total of the element and every descendant.

WBS Element	Description	Budget Head	Status	Progress	Budget	Commitment	Actual CWIP	Recd-Unbilled
CAPEX-2026-001.01	Land and Site Development	Land & Site Development	Technically Completed	100%	no budget	₹0	₹0	₹0
▼ CAPEX-2026-001.02	Civil and Structural Work	Civil	Released	62%	₹25,00,000	₹3,00,000	₹11,00,000	₹0
▼ CAPEX-2026-001.02.01	Foundation and Piling	Civil	Released	90%	at CAPEX-2026-001.02	₹3,00,000	₹11,00,000	₹0
CAPEX-2026-001.02.01.01	Site Piling Works	Civil	Released	100%	at CAPEX-2026-001.02	₹0	₹8,00,000	₹0
CAPEX-2026-001.02.01.02	Foundation Concreting	Civil	Released	80%	at CAPEX-2026-001.02	₹3,00,000	₹3,00,000	₹0
CAPEX-2026-001.02.02	Structural Steel Erection	Civil	Released	45%	at CAPEX-2026-001.02	₹0	₹0	₹0
▼ CAPEX-2026-001.03	Plant and Machinery	Plant & Machinery	Released	48%	₹90,00,000	₹46,50,000	₹24,40,000	₹5,00,000
CAPEX-2026-001.03.01	Rolling Mill Equipment	Plant & Machinery	Released	55%	at CAPEX-2026-001.03	₹39,00,000	₹17,40,000	₹0
CAPEX-2026-001.03.02	Material Handling System	Plant & Machinery	Released	40%	at CAPEX-2026-001.03	₹7,50,000	₹7,00,000	₹5,00,000
CAPEX-2026-001.04	Electrical	Electrical	Released	35%	₹23,00,000	₹3,00,000	₹6,00,000	₹0
CAPEX-2026-001.05	Installation	Installation	Released	20%	₹12,00,000	₹0	₹7,60,000	₹0
CAPEX-2026-001.06	Consultancy and Project Management	Consultancy & Other	Released	55%	₹10,00,000	₹3,00,000	₹3,00,000	₹0
CAPEX-2026-001.07	Instrumentation and Automation	Instrumentation & Automation	Released	10%	no budget	₹0	₹0	₹0
CAPEX-2026-001.08	Design and Engineering	Consultancy &	Released	20%	no budget	₹0	₹0	₹0

The rail with every group expanded; the WBS Hierarchy Explorer for a project.

6. Modules and screens

Work

Screen	Purpose
Executive Dashboard	Portfolio budget, commitment, actual CWIP, available and utilisation per project; exceptions requiring attention.
My Approvals	Everything waiting for your decision: purchase requests, exceptions, revisions, capitalisation.
Alerts & Exceptions	Budget breaches, bills exceeding orders, unbilled receipts, integration exceptions.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entities

All plants

Compact

✓ Approvals 3

⚠ Alerts 3

SA System Administrator Administrator

Notifications

Change password

Sign out

Expand all

Collapse all

WORK

Executive Dashboard

✓ My Approvals 3

⚠ Alerts & Exceptions 3

PROJECT CONTROL

CAPEX Projects

WBS Explorer

Budget Planning Grid

Budget Setup

Budget Availability Check

Budget Revisions

Budget Planning Grid (cells)

Budget Version Comparison

Budget Availability Check (c...

PROCUREMENT & ACTUALS

Purchase Requests

Commitments (PO)

GRN & Receipts

Internal Material Requests

Vendor Bills & CWIP

Commitment Reconciliation

CLOSURE

★ Capitalisation

INTEGRATION

Home > Approvals

My Approval Inbox

3 items awaiting decision

Type	Reference	Value	Detail	
Purchase request — exception	PR-2026-0010	₹20,00,000	Available budget insufficient. Routed for exception approval per PDF section 7.	Approve
Budget revision	REV-003	—	Additional instrumentation scope identified during commissioning readiness review.	Approve
Capitalisation request	CAP-2026-0001	₹0	CAPEX-2026-001 New Production Line	Approve

My Approvals. Each row names the type, reference, value and the reason it is here.

Project Control

Screen	Purpose
CAPEX Projects	The project register with status, plant and budget.
WBS Explorer	The hierarchy of a project, expandable to the control cells.
Budget Planning Grid	Budget by WBS element and budget head; original, revisions, commitment, actual, available.
Budget Setup / Budget Categories	Create the original budget lines of a project by category; maintain categories.
Budget Availability Check	Ask "can I spend this much here?" before raising anything; the same check the system applies.
Budget Revisions	Supplements and transfers with maker-checker approval; the original budget is never overwritten.
Budget Version Comparison	Compare two budget versions cell by cell.

UAT — SYNTHETIC DATA — ZOH0 ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entitiesAll plantsCompactApprovalsAlertsSystem Administrator

NotificationsChange passwordSign out

Home - Budgets

Budget Planning Grid

OriginalBudgetCommitmentAvailable

Project

CAPEX-2026-001 — New Production Line

Budget by WBS element and budget head

WBS	Description	Budget Head	Original	Revisions	Current Approved	PO Commitment	Actual CWP	Available	Exposure %
CAPEX-2026-001-01	Civil and Structural Work	Civil	\$25,00,000	\$0	\$25,00,000	\$0	\$0	\$25,00,000	0.0%
CAPEX-2026-001-02-01	Site Piling Works	Civil	\$0	\$0	\$0	\$0	\$0	\$0	0.0%
CAPEX-2026-001-02-02	Foundation Concreting	Civil	\$0	\$0	\$0	\$3,00,000	\$0	\$0	0.0%
CAPEX-2026-001-03	Plant and Machinery	Plant & Machinery	\$60,00,000	\$10,00,000	\$90,00,000	\$0	\$0	\$90,00,000	0.0%
CAPEX-2026-001-03-01	Rolling Mill Equipment	Plant & Machinery	\$0	\$0	\$0	\$39,00,000	\$17,40,000	\$0	0.0%
CAPEX-2026-001-03-02	Material handling System	Plant & Machinery	\$0	\$0	\$0	\$7,50,000	\$7,00,000	\$0	0.0%
CAPEX-2026-001-04	Electrical	Electrical	\$20,00,000	\$3,00,000	\$23,00,000	\$3,00,000	\$0	\$0	39.1%
CAPEX-2026-001-05	Installation	Installation	\$15,00,000	\$15,00,000	\$12,00,000	\$0	\$7,60,000	\$4,40,000	63.3%
CAPEX-2026-001-06	Consultancy and Project Management	Consultancy & Other	\$10,00,000	\$0	\$10,00,000	\$3,00,000	\$3,00,000	\$4,00,000	60.0%
Total			\$1,50,00,000	\$10,00,000	\$1,60,00,000	\$55,50,000	\$28,00,000	\$32,50,000	67.2%

Each row is one WBS element and one budget head. The original approved budget is immutable — supplements, returns and transfers are recorded as separate versioned lines, each carrying requestor, approver, date, reason and approval reference.

Budget Planning Grid.

UAT — SYNTHETIC DATA — ZOH0 ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entitiesAll plantsCompactApprovalsAlertsSystem Administrator

NotificationsChange passwordSign out

Home - Budgets - Availability Check

Budget Availability Check

Simulate a proposed commitment

Project

WBS element

Budget head

Proposed value (\$)

Run check

Rules, at most two decimal places. The value is sent to the server as an exact decimal string, never as a floating point number.

How the check works

Exposure

Available Budget

Utilisation

Open PO Commitment + Actual CWP

Current Approved Budget + Exposure

Exposure = Current Approved Budget

Budget held on a WBS element covers that element and every descendant, so the check evaluates the rolled-up position. Checking only the element's own line would let a parent's budget look untouched while its children consumed it.

Thresholds warning at 80%, exception approval at 90%, hard stop when exposure exceeds the approved budget.

Budget Availability Check.

UAT — SYNTHETIC DATA — ZOH0 ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entitiesAll plantsCompactApprovalsAlertsSystem Administrator

NotificationsChange passwordSign out

Home - Budgets - Budget Setup

Budget Setup

Budget

Upload budget

Project

Status

All statuses

Apply filters

New Budget

No original budgets match these filters. Use "New Budget" above to create one, or adjust the filters.

Budget Setup.

UAT — SYNTHETIC DATA — ZOH0 ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entitiesAll plantsCompactApprovalsAlertsSystem Administrator

NotificationsChange passwordSign out

Home - Budgets - Revisions

Budget Revisions

Request revision

Budget revisions

Export CSV

Export XLSX

Revision register — the original budget is never overwritten

Revision	Project	Type	Reason	Requested by	Approver	Approval ref	Effective	Value	Status
001	CAPEX-2026-001	SUPPLEMENT	Vendor quote for rolling mill exceeded estimate after steel price revision.	U-PM	V. Agarwal	CAPEX-CORP/2026/004	2026-06-12	\$10,00,000	Approved
002	CAPEX-2026-001	TRANSFER	Scope moved from Installation to Electrical after design review.	U-PM	V. Agarwal	CAPEX-CORP/2026/005	2026-06-22	\$0	Approved
003	CAPEX-2026-001	SUPPLEMENT	Additional instrumentation scope identified during commissioning readiness review.	U-PM	—	—	—	\$0	Submitted

Budget Revisions.

Procurement & Actuals

Screen	Purpose
Purchase Requests	Raise, submit, approve. Budget check and status per request; export headers and lines.
Commitments (PO)	Purchase orders with ordered, billed and open commitment; amend, cancel, close; emit to Zoho ERP.
GRN & Receipts	Goods receipts read from Zoho ERP; received-not-billed exposure.
Internal Material Requests	Material met from stores instead of purchase: request, approve, allocate, issue, return, consume, cancel.
Vendor Bills & CWIP	Bills read from Zoho ERP, posted as actual CWIP.
Commitment Reconciliation	Ordered = received = billed, line by line, with open values and exceptions.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub | All entities | All plants | Compact | Approvals 3 | Alerts 3 | SA System Administrator Administrator | Notifications | Change password | Sign out

Expand all | Collapse all

Home > Purchase Requests

Purchase Requests | Create purchase request | Purchase requests | Export CSV | Export XLSX | Purchase request lines | Export CSV | Export XLSX

Purchase request control view

PR Number	Project	WBS	Budget Head	Description	Value	Budget Check	Status	Approver
PR-2026-0001	CAPEX-2026-001	CAPEX-2026-001.02.01.01	Civil	Piling contractor - 120 piles	₹8,00,000	✓ Within budget	✓ Approved	U-PLH
PR-2026-0002	CAPEX-2026-001	CAPEX-2026-001.02.01.02	Civil	RCC foundation works	₹6,00,000	✓ Within budget	✓ Approved	U-PLH
PR-2026-0003	CAPEX-2026-001	CAPEX-2026-001.03.01	Plant & Machinery	Rolling mill main drive	₹30,00,000	✓ Within budget	✓ Approved	U-CFO
PR-2026-0004	CAPEX-2026-001	CAPEX-2026-001.03.01	Plant & Machinery	Mill stands and guides	₹22,00,000	✓ Within budget	✓ Approved	U-CFO
PR-2026-0005	CAPEX-2026-001	CAPEX-2026-001.03.02	Plant & Machinery	Overhead crane 20T	₹12,00,000	✓ Within budget	✓ Approved	U-CFO
PR-2026-0006	CAPEX-2026-001	CAPEX-2026-001.04	Electrical	HT panels and switchgear	₹9,00,000	✓ Within budget	✓ Approved	U-PLH
PR-2026-0007	CAPEX-2026-001	CAPEX-2026-001.04	Electrical	Cabling and trays	₹5,00,000	✓ Within budget	✓ Approved	U-PLH
PR-2026-0008	CAPEX-2026-001	CAPEX-2026-001.05	Installation	Mechanical erection contractor	₹7,00,000	✓ Within budget	✓ Approved	U-PLH
PR-2026-0009	CAPEX-2026-001	CAPEX-2026-001.06	Consultancy & Other	Detailed engineering consultancy	₹6,00,000	✓ Within budget	✓ Approved	U-FIN
PR-2026-0010	CAPEX-2026-001	CAPEX-2026-001.03.02	Plant & Machinery	Conveyor system - additional scope	₹20,00,000	✗ Exceeds budget	! Exception Pending	—
PR-2026-0011	CAPEX-2026-002	CAPEX-2026-002.01	Civil	Warehouse shed civil	₹28,00,000	✓ Within budget	✓ Approved	U-PLH
PR-2026-0012	CAPEX-2026-002	CAPEX-2026-002.02	Plant & Machinery	Pallet racking system	₹14,00,000	✓ Within budget	✓ Approved	U-PLH
PR-2026-0013	CAPEX-2026-003	CAPEX-2026-003.01	Plant & Machinery	Solar modules 2 MW	₹22,00,000	✓ Within budget	✓ Approved	U-CFO
PR-2026-0014	CAPEX-2026-003	CAPEX-2026-003.02	Electrical	Inverters and transformers	₹9,00,000	✓ Within budget	✓ Approved	U-PLH
PR-2026-0015	CAPEX-2026-001	CAPEX-2026-001.02.02	Civil	Structural steel supply	₹9,00,000	✓ Within budget	Submitted	—
PR-2026-0016	CAPEX-2026-001	CAPEX-2026-001.07	Instrumentation & Automation	PLC and SCADA package	₹4,00,000	✓ Within budget	Submitted	—

Purchase Requests with the two export controls (headers and lines) and the Approve action on rows awaiting a decision.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub | All entities | All plants | Compact | Approvals 3 | Alerts 3 | SA System Administrator Administrator | Notifications | Change password | Sign out

Expand all | Collapse all

Home > Commitments

Commitments — Purchase Orders | Raise purchase order | Purchase order lines | Export CSV | Export XLSX

Purchase order commitment view

PO Number	Vendor	Project	Status	Curr.	Ordered	Billed	Open Commitment	Amend	Actions
PO-2026-0001	Cosha Piling Works Pvt Ltd	CAPEX-2026-001	Fully Activated	INR	₹8,00,000	₹8,00,000	₹0	Amend	Cancel
Line 1 - CAPEX-2026-001.02.01.01	Piling - 120 nos				₹8,00,000	₹8,00,000	₹0	Fully billed	
PO-2026-0002	Korark Constructions	CAPEX-2026-001	Partially Activated	INR	₹6,00,000	₹3,00,000	₹3,00,000	Amend	Cancel
Line 2 - CAPEX-2026-001.02.01.01	RCC foundation				₹6,00,000	₹3,00,000	₹3,00,000	Partially billed	
PO-2026-0003	Bharat Heavy Engineering Co	CAPEX-2026-001	Partially Activated	INR	₹14,00,000	₹17,00,000	₹17,00,000	Amend	Cancel
Line 3 - CAPEX-2026-001.02.01.01	Rolling mill main drive				₹14,00,000	₹17,00,000	₹17,00,000	Partially billed	
PO-2026-0004	Bharat Heavy Engineering Co	CAPEX-2026-001	Fully Committed	INR	₹22,00,000	₹0	₹22,00,000	Amend	Cancel
Line 4 - CAPEX-2026-001.03.01	M&I stands and guides				₹22,00,000	₹0	₹22,00,000	PO approved, not billed	
PO-2026-0005	Eastern Crane Ltd	CAPEX-2026-001	Partially Activated	INR	₹12,00,000	₹7,00,000	₹5,00,000	Amend	Cancel
Line 5 - CAPEX-2026-001.03.02	Overhead crane 20T				₹12,00,000	₹7,00,000	₹5,00,000	Partially billed	
PO-2026-0006	Urul Electricals	CAPEX-2026-001	Partially Activated	INR	₹9,00,000	₹6,00,000	₹3,00,000	Amend	Cancel
Line 6 - CAPEX-2026-001.04	HT panel				₹9,00,000	₹6,00,000	₹3,00,000	Fully billed	
Line 7 - CAPEX-2026-001.04	LT switchgear				₹9,00,000	₹0	₹9,00,000	PO approved, not billed	
PO-2026-0007	Urul Electricals	CAPEX-2026-001	Cancelled	INR	₹5,00,000	₹0	₹0	Released	
Line 8 - CAPEX-2026-001.04	Cabling and trays				₹5,00,000	₹0	₹0	PO cancelled before billing	
PO-2026-0008	Sreen Electrics	CAPEX-2026-001	Fully Committed	INR	₹7,00,000	₹7,00,000	₹0	Amend	Cancel

Commitments (PO).

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub | All entities | All plants | Compact | Approvals 3 | Alerts 3 | SA System Administrator Administrator | Notifications | Change password | Sign out

Expand all | Collapse all

Home > GRN and Receipts

GRN & Unbilled Receipts | Goods receipt lines | Export CSV | Export XLSX

Goods receipts

GRN	PO	Received	Type	Value	Lines
GRN-2026-0001	PO-2026-0001	2026-07-10	Receipt	₹8,00,000	CAPEX-2026-001.02.01.01 × 1
GRN-2026-0002	PO-2026-0002	2026-07-12	Receipt	₹4,20,000	CAPEX-2026-001.02.01.02 × 0.7
GRN-2026-0003	PO-2026-0003	2026-07-15	Receipt	₹17,00,000	CAPEX-2026-001.03.01 × 0.5
GRN-2026-0004	PO-2026-0004	2026-07-18	Receipt	₹12,00,000	CAPEX-2026-001.03.02 × 1
GRN-2026-0005	PO-2026-0005	2026-07-20	Receipt	₹6,00,000	CAPEX-2026-001.04 × 1
GRN-2026-0006	PO-2026-0006	2026-07-22	Receipt	₹13,00,000	CAPEX-2026-001.06 × 0.5
GRN-2026-0007	PO-2026-0007	2026-07-25	Receipt	₹16,80,000	CAPEX-2026-002.01 × 0.6
GRN-2026-0008	PO-2026-0012	2026-07-28	Receipt	₹11,00,000	CAPEX-2026-003.01 × 0.5
GRN-2026-0009	PO-2026-0002	2026-07-30	Reversal	(₹1,20,000)	CAPEX-2026-001.02.01.02 × -0.2

1 Zoho ERP purchase-receive lines carry no link back to a purchase order line, no project or WBS coding, and the module exposes no list endpoint. Received QAS users will require but unbilled exposure is therefore reconstructed inside this application rather than read from Zoho.

GRN & Receipts.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entitiesAll plantsCompactApprovals3Alerts3SASystem AdministratorAdministratorNotificationsChange passwordSign out

Expand allCollapse all

WORK

- Executive Dashboard
- My Approvals3
- Alerts & Exceptions3

PROJECT CONTROL

- CAPEX Projects
- WBS Explorer
- Budget Planning Grid
- Budget Setup
- Budget Availability Check
- Budget Revisions
- Budget Planning Grid (cells)
- Budget Version Comparison
- Budget Availability Check (c...

PROCUREMENT & ACTUALS

- Purchase Requests
- Commitments (PO)
- GRN & Receipts
- Internal Material Requests
- Vendor Bills & CWIP
- Commitment Reconciliation

CLOSURE

- Capitalisation

INTEGRATION

Home > Internal Material Requests

Internal Material Requests

ProjectStatus

All projectsAll statusesApply filtersInternal material requestsExport CSVExport XLSXInternal material movementsExport CSVExport XLSX

Number	PR	WBS	Item	Req. Appr.	Alloc.	Issued	Returned	Consumed	Valuation	Allocation %	Consumption %	Status	Mapping
206-0001	PR-0001	CAPEX-2026-001.01	synthetic cable drum (penck)	2	2	0	0	0	MANUAL	0	0	✖ CANCELLED	✓ Mapped View
										₹1,000,000	100		

Internal Material Requests.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entitiesAll plantsCompactApprovals3Alerts3SASystem AdministratorAdministratorNotificationsChange passwordSign out

Expand allCollapse all

WORK

- Executive Dashboard
- My Approvals3
- Alerts & Exceptions3

PROJECT CONTROL

- CAPEX Projects
- WBS Explorer
- Budget Planning Grid
- Budget Setup
- Budget Availability Check
- Budget Revisions
- Budget Planning Grid (cells)
- Budget Version Comparison
- Budget Availability Check (c...

PROCUREMENT & ACTUALS

- Purchase Requests
- Commitments (PO)
- GRN & Receipts
- Internal Material Requests
- Vendor Bills & CWIP
- Commitment Reconciliation

CLOSURE

- Capitalisation

INTEGRATION

Home > Vendor Bills

Vendor Bills & Actual CWIP

Vendor bill linesExport CSVExport XLSX

Vendor bills posted to CWIP

Bill	PO	Vendor	Due	Type	Value	WBS coding
Bill-2026-0001	PO-2026-0001	Cochin Piling Works Pvt Ltd	2026-07-14	Bill	₹8,00,000	CAPEX-2026-001.02.01.01 - Civil
Bill-2026-0002	PO-2026-0002	Korark Constructors	2026-07-16	Bill	₹3,00,000	CAPEX-2026-001.02.01.02 - Civil
Bill-2026-0003	PO-2026-0003	Bharat Heavy Engineering Co	2026-07-20	Bill	₹17,40,000	CAPEX-2026-001.03.01 - Plant & Machinery
Bill-2026-0004	PO-2026-0004	Eastern Cranes Ltd	2026-07-24	Bill	₹7,50,000	CAPEX-2026-001.03.02 - Electrical
Bill-2026-0005	PO-2026-0005	Utkal Electricals	2026-07-26	Bill	₹6,00,000	CAPEX-2026-001.04 - Electrical
Bill-2026-0006	PO-2026-0006	Delta Engineering Consultants	2026-07-28	Bill	₹3,00,000	CAPEX-2026-001.06 - Consultancy & Other
Bill-2026-0007	PO-2026-0007	Korark Constructors	2026-07-29	Bill	₹16,80,000	CAPEX-2026-002.01 - Civil
Bill-2026-0008	PO-2026-0008	Sunpeak Energy GmbH	2026-07-30	Bill	₹19,00,000	CAPEX-2026-003.01 - Plant & Machinery
Bill-2026-0009	PO-2026-0009	Eastern Cranes Ltd	2026-08-02	Bill	₹750,000	CAPEX-2026-001.03.01 - Plant & Machinery
Bill-2026-0010	PO-2026-0010	Srinam Erectors	2026-08-03	Bill	₹7,60,000	CAPEX-2026-001.05 - Installation

Bill lines carry purchase order, Item, & Zoho ERP, so commitment-to-actual conversion is matched at line level and a purchase order can never be counted twice.

Vendor Bills & CWIP.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entitiesAll plantsCompactApprovals3Alerts3SASystem AdministratorAdministratorNotificationsChange passwordSign out

Expand allCollapse all

WORK

- Executive Dashboard
- My Approvals3
- Alerts & Exceptions3

PROJECT CONTROL

- CAPEX Projects
- WBS Explorer
- Budget Planning Grid
- Budget Setup
- Budget Availability Check
- Budget Revisions
- Budget Planning Grid (cells)
- Budget Version Comparison
- Budget Availability Check (c...

PROCUREMENT & ACTUALS

- Purchase Requests
- Commitments (PO)
- GRN & Receipts
- Internal Material Requests
- Vendor Bills & CWIP
- Commitment Reconciliation

CLOSURE

- Capitalisation

INTEGRATION

Home > Reconciliation

Commitment-to-Actual Reconciliation

Reconciliation exceptionsExport CSVExport XLSX

LinesOpen commitmentBilledReceived not billedExceptions

16₹1,00,70,000₹79,80,000₹5,00,0002

Line-level reconciliation — purchase order — receipt — bill


PO	WBS	Description	Ordered	Received	Billed	Open Commitment	Recd-Unbilled	Exposure	Position
PO-2026-0001	CAPEX-2026-001.02.01.01	Piling - 120 nos	₹8,00,000	₹8,00,000	₹8,00,000	₹0	₹0	₹8,00,000	Fully billed
PO-2026-0002	CAPEX-2026-001.02.01.02	RCC foundation	₹6,00,000	₹3,00,000	₹3,00,000	₹3,00,000	₹0	₹6,00,000	Partially billed
PO-2026-0003	CAPEX-2026-001.03.01	Rolling mill main drive	₹34,40,000	₹17,00,000	₹17,40,000	₹17,00,000	₹0	₹34,40,000	Partially billed
PO-2026-0004	CAPEX-2026-001.03.01	Mill stands and guides	₹22,00,000	₹0	₹0	₹22,00,000	₹0	₹22,00,000	PO approved, not billed
PO-2026-0005	CAPEX-2026-001.03.02	Overhead crane 20T	₹12,50,000	₹12,00,000	₹7,00,000	₹5,50,000	₹5,00,000	₹12,50,000	✖ Partially billed
PO-2026-0006	CAPEX-2026-001.04	HT panel	₹6,00,000	₹6,00,000	₹6,00,000	₹0	₹0	₹6,00,000	Fully billed
PO-2026-0006	CAPEX-2026-001.04	LT switchgear	₹3,00,000	₹0	₹0	₹3,00,000	₹0	₹3,00,000	PO approved, not billed
PO-2026-0007	CAPEX-2026-001.04	Cabling and trays	₹5,00,000	₹0	₹0	₹0	₹0	₹0	✖ PO cancelled before billing
PO-2026-0008	CAPEX-2026-001.05	Mechanical erection	₹7,00,000	₹0	₹7,60,000	₹0	₹0	₹7,60,000	✖ Bill exceeds PO
PO-2026-0009	CAPEX-2026-001.06	Detailed engineering	₹6,00,000	₹3,00,000	₹3,00,000	₹3,00,000	₹0	₹6,00,000	Partially billed
PO-2026-0010	CAPEX-2026-002.01	Warehouse shed civil	₹28,00,000	₹16,80,000	₹16,80,000	₹11,20,000	₹0	₹28,00,000	Partially billed
PO-2026-0011	CAPEX-2026-002.02	Pallet racking	₹14,00,000	₹0	₹0	₹14,00,000	₹0	₹14,00,000	PO approved, not billed
PO-2026-0012	CAPEX-2026-003.01	Solar modules 2 MW	₹22,00,000	₹11,00,000	₹11,00,000	₹11,00,000	₹0	₹22,00,000	Partially billed
PO-2026-0013	CAPEX-2026-003.02	Inverters and transformers	₹9,00,000	₹0	₹0	₹9,00,000	₹0	₹9,00,000	PO approved, not billed
PO-2026-0014	CAPEX-2026-001.02.01.01	Additional piling - provisional	₹2,00,000	₹0	₹0	₹0	₹0	₹0	✖ PO closed - residual released

Commitment-to-Actual Reconciliation.

Closure

Synthetic data · Zoho ERP demo tenant 60074128927 · build 63b07c6


Page 12 of 26

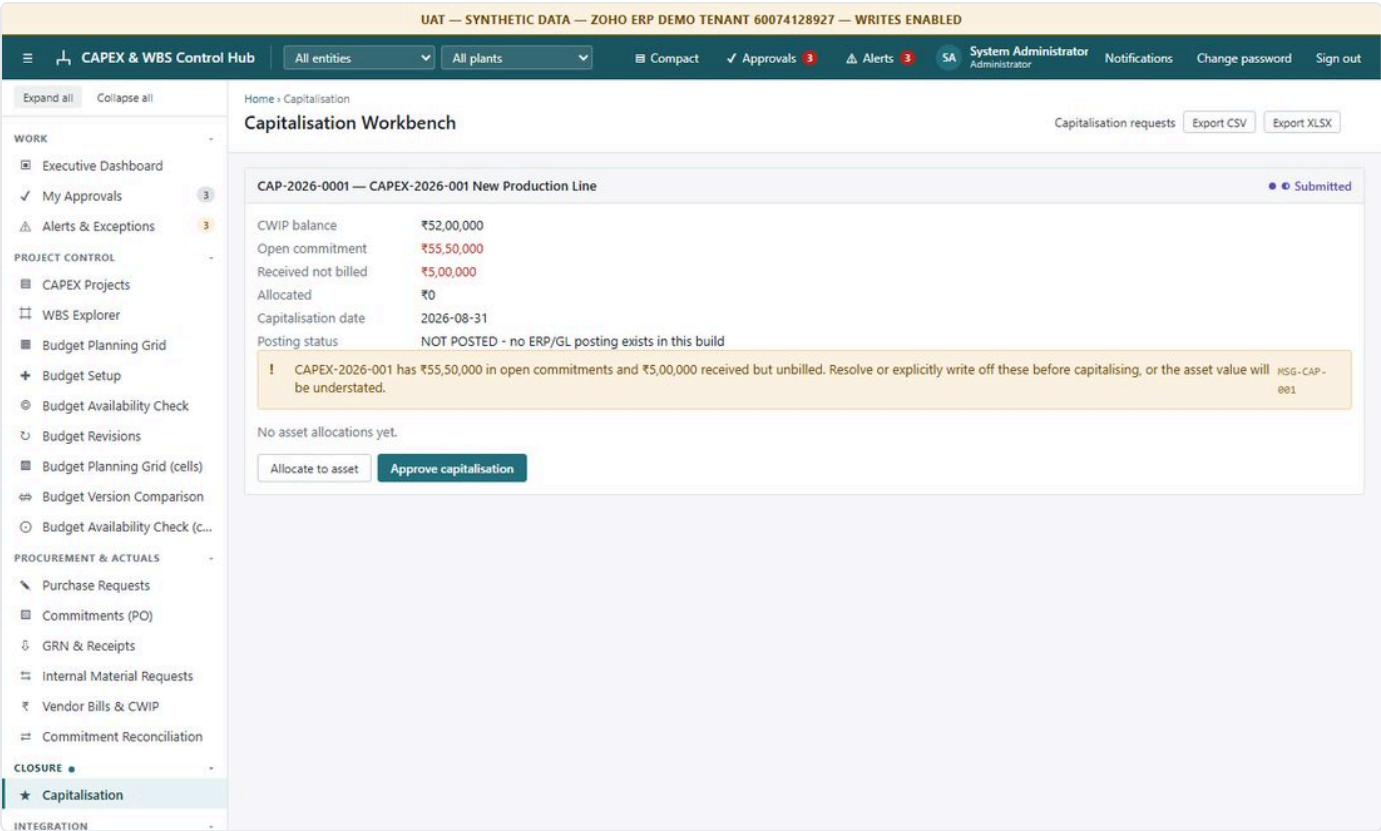


Capitalisation Workbench: allocate CWIP to assets, then approve capitalisation (CapitalisationApprover).

Approval engine (routable screens)


Reached by link from My Approvals or directly: **My Approval Inbox, Approval Request Detail, Approval Timeline, Escalation & SLA Monitor, Approval Matrix Configuration, Workflow Version History, Approval Rule Simulator, Delegation Management.**

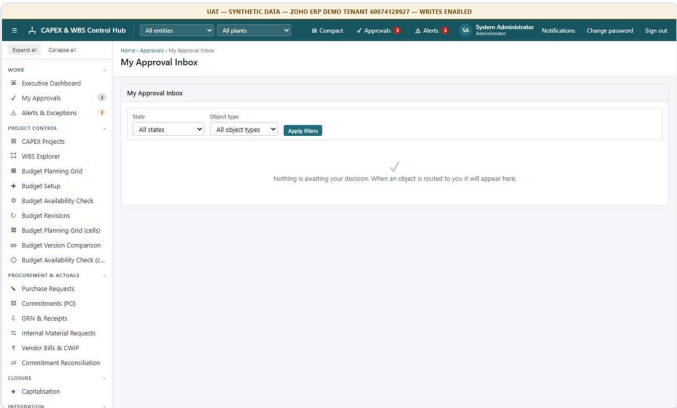


My Approval Inbox.

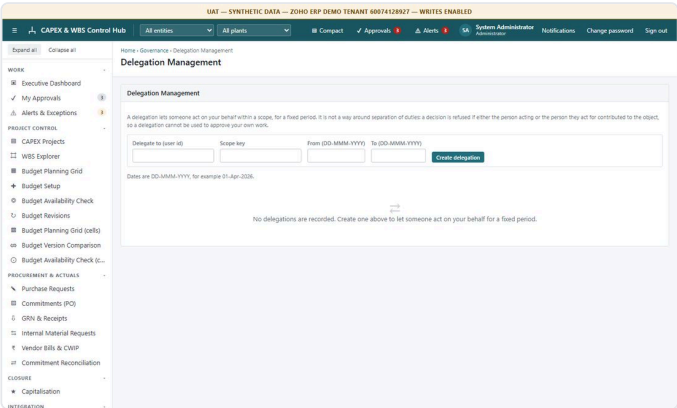

Delegation Management: delegate an authority you hold, for a period, to someone independent of the object.

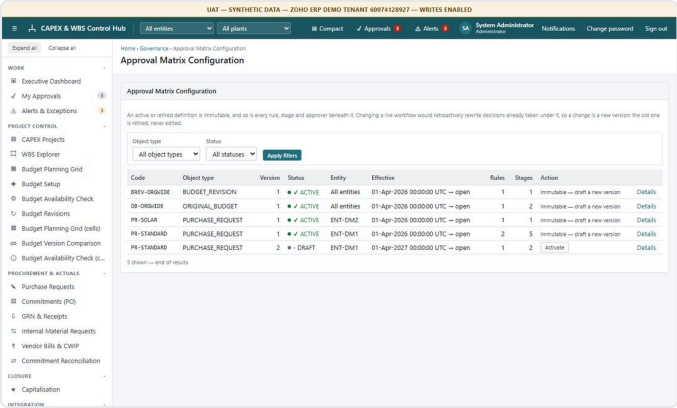


Approval Matrix Configuration.

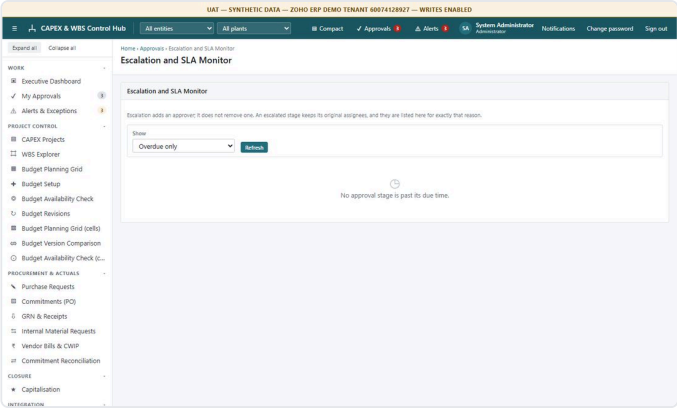


Escalation & SLA Monitor.

Integration, Governance, Analytics, Settings

Screen	Purpose
Zoho ERP Connector / API Inventory	Connection state and mode, token health, sweeps, order adoption, the API operations the product uses.
Integration Mapping	Master-data and transaction field mapping workbenches; sync direction; connector audit and credential log.
Audit Trail	Every entry, filterable by stream, object, action and actor; chain verification.
Notifications (Governance)	The Administrator's outbox: counts by state, filters, delivery attempts, dispatch, retry.
Analytics	Executive dashboard, controller workbench, project list and object pages, WBS tree, CWIP ledger, commitment and CWIP ageing, exception monitor.
Settings & Master Data / Exchange Rates	Organisation hierarchy, item and vendor masters, exchange-rate book.

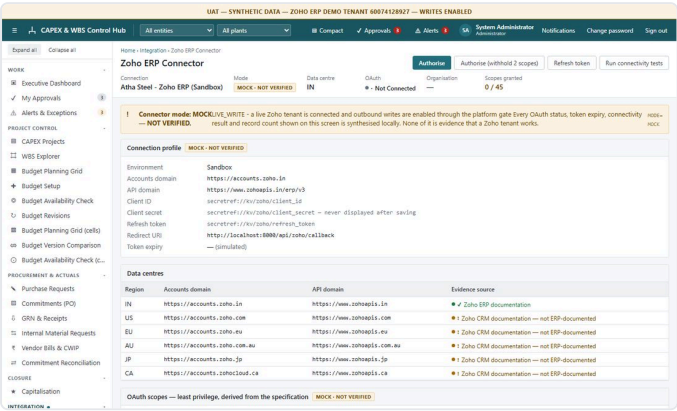

Zoho ERP Connector.

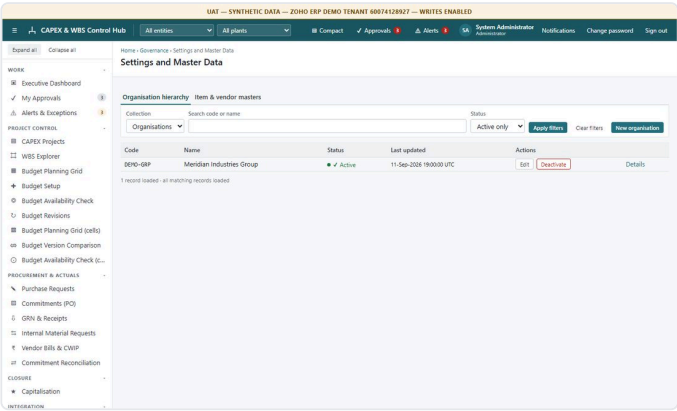

Settings and Master Data.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entities

All plants

Compact

Approvals 3

Alerts 3

SA System Administrator Administrator

Notifications

Change password

Sign out

Expand allCollapse all

WORK

Executive Dashboard

My Approvals3

Alerts & Exceptions3

PROJECT CONTROL

CAPEX Projects

WBS Explorer

Budget Planning Grid

Budget Setup

Budget Availability Check

Budget Revisions

Budget Planning Grid (cells)

Budget Version Comparison

Budget Availability Check (c...

PROCUREMENT & ACTUALS

Purchase Requests

Commitments (PO)

GRN & Receipts

Internal Material Requests

Vendor Bills & CWIP

Commitment Reconciliation

CLOSURE

Capitalisation

INTEGRATION

Home > Governance > Exchange Rates

Exchange Rates

SourceTargetStatusEffective fromEffective toImport...+ New rate

USDINRAll statusesdd-mm-yyyydd-mm-yyyyApply

Pair	Rate	Source	Effective	Status	Created by	Activated by	Actions
USD/INR	83.90000000	RBI_REFERENCE	07-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
KWD/INR	273.05000000	RBI_REFERENCE	07-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
JPY/INR	0.56500000	RBI_REFERENCE	07-Aug-2026	Awaiting activation	U-FIN	—	HistoryActivate
EUR/INR	97.95000000	RBI_REFERENCE	07-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
USD/INR	83.77000000	RBI_REFERENCE	05-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
KWD/INR	272.60000000	RBI_REFERENCE	05-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
JPY/INR	0.56200000	RBI_REFERENCE	05-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
EUR/INR	97.91000000	RBI_REFERENCE	05-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
EUR/INR	98.10000000	RBI_REFERENCE	05-Aug-2026	Superseded	U-FIN	U-ADM	History
USD/INR	83.81000000	RBI_REFERENCE	04-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
KWD/INR	272.80000000	RBI_REFERENCE	04-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
JPY/INR	0.56300000	RBI_REFERENCE	04-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
EUR/INR	97.80000000	RBI_REFERENCE	04-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
USD/INR	83.72000000	RBI_REFERENCE	03-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
KWD/INR	272.45000000	RBI_REFERENCE	03-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
JPY/INR	0.56100000	RBI_REFERENCE	03-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire
EUR/INR	97.64000000	RBI_REFERENCE	03-Aug-2026	Active	U-FIN	U-ADM	HistoryRetire

Exchange Rates (FinanceApprover maintains; everyone else reads).

7. How to operate: the core procedures

7.1 Raise and approve a purchase request

1. **Requestor / BudgetController**: Purchase Requests → **Create purchase request**. Choose project, WBS element, budget head, describe the need and enter the value. Save (Draft), then **Submit**.
2. On submission the system checks the control cell. Within budget → status **Submitted**, routed to a ProcurementApprover. Over budget → status **Exception Pending**, routed to a FinanceApprover; the shortfall is shown and the reason is mandatory.
3. **Approver**: My Approvals or the register → **Approve** (or reject with a reason). You cannot approve a request you raised or edited: the server refuses with *SELF_APPROVAL*. An Administrator may override this deliberately (section 8).
4. Approved requests reserve budget (PR reserve) until converted or released.

7.2 Convert to a purchase order and emit to Zoho ERP

1. Commitments (PO) → **Raise purchase order** from an approved request; choose vendor and currency (INR by default; a foreign currency needs a rate from the rate book, otherwise the order is refused as *FX_RATE_UNAVAILABLE*).
2. The order commits budget (open commitment) and releases the request's reserve.
3. **Emit** sends the order to the Zoho ERP demo tenant once; the outbox row keeps the external id, and an identical retry creates nothing new. Every emitted order carries the CAPEX reference, WBS code and budget head as custom fields.
4. Amend, cancel and close are ProcurementApprover actions on the order row.

7.3 Receipts, bills and reconciliation

Receipts and vendor bills are read from Zoho ERP by the sweeps (Zoho ERP Connector → sweeps, or the scheduled run). A receipt moves value to received-not-billed; a bill posts actual CWIP and reduces open commitment. Commitment Reconciliation shows ordered, received, billed and open per line and raises coded exceptions (for example an unattributed receipt line, a foreign-currency bill without a rate basis, an order whose dimensions do not match).

7.4 Internal material requests (material from stores)

1. On a purchase-request line, a **fulfilment decision** (BudgetController or ProcurementApprover) chooses External purchase, Internal transfer, or Split with an internal quantity. Internal material needs a valuation: from the inventory provider when mapped, otherwise a manual unit rate with a written note.
2. The decision raises the internal material request (**REQUESTED**). Approve (ProcurementApprover; maker-checker applies) → **APPROVED**.
3. **Allocate** moves the money from the request's reserve to internal allocation; **Issue** moves it to internal consumption (CWIP); **Return** gives it back; **Consume** confirms use; **Transfer** moves stock between stores without money; **Cancel** releases everything while still reserved.
4. Only the external portion of a split line converts to a purchase order; a fully internal line cannot be converted.

7.5 Budget revisions

Budget Revisions → **Request revision** (Supplement or Transfer, with reason). A FinanceApprover approves; the original budget stays visible and the revision is a separate line. Transfers need both cells in your scope.

7.6 Capitalisation

Capitalisation → allocate CWIP to assets (BudgetController or FinanceApprover) → **Approve capitalisation** (CapitalisationApprover). A project with open commitment is blocked with *CAPITALISATION_BLOCKED* until the commitment is closed.

8. Administrator tasks

8.1 The deliberate self-approval override

When an Administrator approves an object it raised or edited, the server first refuses with *SELF_APPROVAL*. The dialog then shows an unmissable warning and asks for a reason of at least 10 characters. Confirming re-sends the approval with the reason. The result:

- the approval is applied;
- an audit entry **ADMIN_SELF_APPROVAL_OVERRIDE** records who, when, the object and the reason;
- every other Administrator is notified.

The override cannot be delegated and is never offered for period reopening. Use it only when no independent approver exists.

8.2 Releasing a password-reset link on UAT

While mail is recorded rather than sent, the only copy of a reset link is in the notification outbox and its body is hidden even from Administrators. If the platform owner has enabled the UAT reveal switch, open Governance → Notifications, find the **PASSWORD_RESET_REQUESTED** row for the user, open it and pass the link to the person. Every reveal is recorded in the audit trail as **NOTIFICATION_BODY_REVEALED** against your name. The switch stops working the moment real mail is enabled.

8.3 Dispatching the outbox

Governance → Notifications → **Dispatch due notifications** sends everything queued or due for retry. Nothing is sent inside a business transaction; dispatch is separate and safe to repeat (a second dispatch claims nothing). When the owner sets the dispatch interval, the ticker does this every minute.

8.4 Linking a Zoho identity to a user

Once single sign-on is configured, a person's Zoho identity must be linked to their existing WBS user before "Continue with Zoho" works for them; an unlinked sign-in is refused and audited. Linking is an Administrator API action (`POST /api/admin/users/{user_id}/identities` with the Zoho subject). No user is ever created by a Zoho sign-in, and no role ever comes from Zoho.

8.5 Delegations

Delegation Management lets an approver delegate an authority they hold, for a period, to someone who is independent of the object. A delegate who contributed to the object is refused exactly as the maker would be.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entitiesAll plants

Compact

Approvals3

Alerts3

SASystem AdministratorAdministrator

Notifications

Change password

Sign out

Expand allCollapse all

WORK

Executive Dashboard

My Approvals3

Alerts & Exceptions3

PROJECT CONTROL

CAPEX Projects

WBS Explorer

Budget Planning Grid

Budget Setup

Budget Availability Check

Budget Revisions

Budget Planning Grid (cells)

Budget Version Comparison

Budget Availability Check (c...

PROCUREMENT & ACTUALS

Purchase Requests

Commitments (PO)

GRN & Receipts

Internal Material Requests

Vendor Bills & CWIP

Commitment Reconciliation

CLOSURE

Capitalisation

INTEGRATION

Home > Notifications

Notifications

Notification outlook

StateEventRecipient user id

All states

Apply filters

Dispatch due notifications

QUEUED11

SENDING0

SENT3

FAILED0

DEAD0

SUPPRESSED0

ADAPTERrecording

AVAILABILITYAvailable

Oldest item due: 2026-09-14T07:19:22.441177+00:00

Event	Recipient	Subject	State	Attempts	Next attempt	Created	
ADMIN_SELF_APPROVAL_OVERRIDE	U-SURAJ	[WBS] Administrator self-approval override on IMR-0001	QUEUED	0/5	2026-09-14T07:21:53.090789+00:00	2026-09-14T07:21:53.090789+00:00	View
ADMIN_SELF_APPROVAL_OVERRIDE	U-RAKESH	[WBS] Administrator self-approval override on IMR-0001	QUEUED	0/5	2026-09-14T07:21:53.090789+00:00	2026-09-14T07:21:53.090789+00:00	View
ADMIN_SELF_APPROVAL_OVERRIDE	U-PRITHA	[WBS] Administrator self-approval override on IMR-0001	QUEUED	0/5	2026-09-14T07:21:53.090789+00:00	2026-09-14T07:21:53.090789+00:00	View
IMR_APPROVED	U-ADM	[WBS] Internal material request IMR-0001 approved	QUEUED	0/5	2026-09-14T07:21:53.090789+00:00	2026-09-14T07:21:53.090789+00:00	View
ADMIN_SELF_APPROVAL_OVERRIDE	U-ABHISHEK	[WBS] Administrator self-approval override on IMR-0001	QUEUED	0/5	2026-09-14T07:21:53.090789+00:00	2026-09-14T07:21:53.090789+00:00	View
ADMIN_SELF_APPROVAL_OVERRIDE	U-SURAJ	[WBS] Administrator self-approval override on PR-0003	QUEUED	0/5	2026-09-14T07:19:23.513400+00:00	2026-09-14T07:19:23.513400+00:00	View
ADMIN_SELF_APPROVAL_OVERRIDE	U-ABHISHEK	[WBS] Administrator self-approval override on PR-0003	QUEUED	0/5	2026-09-14T07:19:23.513400+00:00	2026-09-14T07:19:23.513400+00:00	View
ADMIN_SELF_APPROVAL_OVERRIDE	U-PRITHA	[WBS] Administrator self-approval override on PR-0003	QUEUED	0/5	2026-09-14T07:19:23.513400+00:00	2026-09-14T07:19:23.513400+00:00	View
ADMIN_SELF_APPROVAL_OVERRIDE	U-RAKESH	[WBS] Administrator self-approval override on PR-0003	QUEUED	0/5	2026-09-14T07:19:23.513400+00:00	2026-09-14T07:19:23.513400+00:00	View
PR_APPROVED	U-ADM	[WBS] Purchase request PR-0003 approved	QUEUED	0/5	2026-09-14T07:19:23.513400+00:00	2026-09-14T07:19:23.513400+00:00	View
PR_SUBMITTED	U-PLH	[WBS] Purchase request PR-0003 awaits your approval	QUEUED	0/5	2026-09-14T07:19:22.441177+00:00	2026-09-14T07:19:22.441177+00:00	View

Governance → Notifications: the Administrator's outbox with filters, counts by state and the Dispatch action.

Synthetic data · Zoho ERP demo tenant 60074128927 · build 63b07c6

Page 19 of 26

9. Exports (CSV and Excel)

Every register, dashboard and closure list carries an export control in the page actions, named after its dataset (for example *Purchase requests* and *Purchase request lines* on the same screen). Press **Export CSV** or **Export XLSX**. The export runs as a job that your browser drives; keep the page open until **Download** appears, then click it. The entity and plant filters in the top bar are applied to the export.

- The Excel workbook has four sheets: Summary, Data, Applied Filters, Metadata. Money cells are numbers in Indian format with a SUM total; dates are real dates in UTC; text is text.
- Excel is capped at 20,000 rows; a larger export is refused honestly. Use CSV or narrow the filters.
- An export job expires after a day; run it again if the download has gone.

Create purchase request

Purchase requests

Export CSV

Export XLSX

Purchase request lines

Export CSV


Export XLSX

The export controls on Purchase Requests.

10. Notifications

Notifications in the top bar opens your preferences and your own delivery history. You can switch off informational events; security notices (password reset, password changed, identity linked, Administrator override) cannot be switched off. Events wired today: PR submitted, PR approved, IMR approved, Administrator self-approval override, export completed, exception raised, password reset requested, password changed, identity linked.

On UAT every notification is **recorded**, not sent. Delivery rows show *RECORDED*. E-mail leaves the platform only after the owner verifies a sender domain and switches the adapter (section 14).

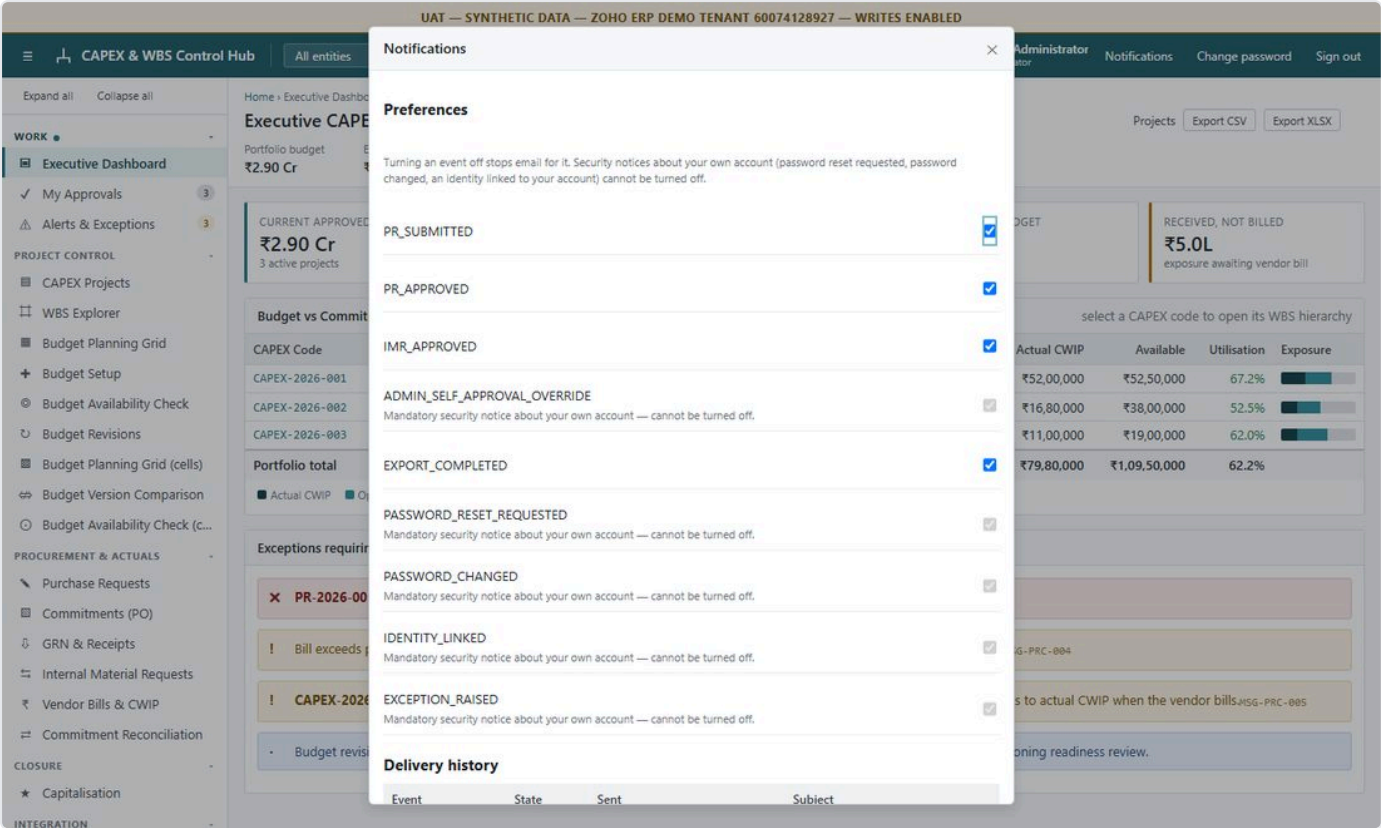

Your notification preferences and history.

11. Governance: audit trail and controls

Governance → Audit Trail lists every entry, filterable by stream, object type and id, action and actor, with a table and a timeline view. **Verify** checks the hash chain of a stream. The chain is intact; the daily anchor that signs each day's chain (a scheduled Catalyst function) is not yet running on UAT, so verification reports *NEVER_ANCHORED*. That is a scheduling gap, not tampering.

UAT — SYNTHETIC DATA — ZOHO ERP DEMO TENANT 60074128927 — WRITES ENABLED

CAPEX & WBS Control Hub

All entities

All plants

Compact

Approvals 3

Alerts 3

SA System Administrator Administrator

Notifications

Change password

Sign out

Expand allCollapse all

WORK

Executive Dashboard

My Approvals3

Alerts & Exceptions3

PROJECT CONTROL

CAPEX Projects

WBS Explorer

Budget Planning Grid

Budget Setup

Budget Availability Check

Budget Revisions

Budget Planning Grid (cells)

Budget Version Comparison

Budget Availability Check (c...

PROCUREMENT & ACTUALS

Purchase Requests

Commitments (PO)

GRN & Receipts

Internal Material Requests

Vendor Bills & CWIP

Commitment Reconciliation

CLOSURE

Capitalisation

INTEGRATION

Home > Governance > Audit Trail Viewer

Audit Trail Viewer

Audit stream

Object type

Object ID

Action

Actor

All streams

Apply filters

Clear filters

Select a single audit stream above to verify its hash chain.

Table

Timeline

Re-verify chain

Seq	Timestamp	Actor	Action	Object	Detail	Entry hash	
6	14-Sep-2026 07:27:20 UTC	U-RAKESH	GRN_MIRRORED	GoodsReceipt GRN-F4201F0C87F595CF1264	Receive 3912780000000074010 line 3912780000000085012 mirrored from ZOHO_ERP onto...	e09c5f14...67ef69	Details
12	14-Sep-2026 07:27:18 UTC	U-RAKESH	GRN_MIRRORED	GoodsReceipt GRN-D8A47088BC6C360E954B	Receive 3912780000000086010 line 3912780000000085005 mirrored from ZOHO_ERP onto...	afc2e1ee...538d7e	Details
11	14-Sep-2026 07:27:18 UTC	U-RAKESH	GRN_MIRRORED	GoodsReceipt GRN-D8A47088BC6C360E954B	Receive 3912780000000086010 line 3912780000000085004 mirrored from ZOHO_ERP onto...	1e00d9e4...141dc5	Details
6	14-Sep-2026 07:27:17 UTC	U-RAKESH	GRN_MIRRORED	GoodsReceipt GRN-5278F9E1E902712D52E6	Receive 3912780000000116003 line 3912780000000109007 mirrored from ZOHO_ERP onto...	d55d4522...c40e92	Details
4	14-Sep-2026 07:21:53 UTC	U-ADM	IMR_CANCELLED	InternalMaterialRequest IMR-38143AF1E04E	IMR-0001 cancelled: smoke 2026-09-14 clean-up: synthetic request withdrawn; 0 pa...	61c156de...4c0622	Details
3	14-Sep-2026 07:21:53 UTC	U-ADM	IMR_APPROVED	InternalMaterialRequest IMR-38143AF1E04E	IMR-0001 approved for 2 of 2; reason: smoke	428a1818...fa052c	Details
2	14-Sep-2026 07:21:53 UTC	U-ADM	ADMIN_SELF_APPROVAL_OVERRIDE ADMIN OVERRIDE	InternalMaterialRequest IMR-38143AF1E04E	{ "actor_user_id": "U-ADM", "amount_paise": 200000, "correlation_id": "f4ed7c6c-b..."	53303bcb...551a27	Details
1	14-Sep-2026 07:21:29 UTC	U-ADM	IMR_REQUESTED	InternalMaterialRequest IMR-38143AF1E04E	IMR-0001 raised for 2 of line 1 of PR-0003 on (CAPEX-DEMO-001.03, BH-DM1-ELEC); ...	2c53d0f4...279c8a	Details
	14-Sep-2026			PurchaseRequest PR-	Line 1 of PR-0003: SPLIT_FULFILMENT;	b87c0a53	

Audit Trail Viewer with filters. Override entries appear under action ADMIN_SELF_APPROVAL_OVERRIDE.

Other controls testers will meet: budget-head isolation (money never moves between heads without a revision), ordered ancestor locking (concurrent approvals on the same cells cannot double-spend), idempotency keys on every write, and refusals with a code and a sentence rather than a silent failure.

Synthetic data · Zoho ERP demo tenant 60074128927 · build 63b07c6

Page 22 of 26

12. Zoho ERP integration

Direction	What	How
Outbound	Purchase orders	Emitted once per approved order to demo tenant 60074128927 with CAPEX reference, WBS code and budget head; duplicates impossible by design. No bill, receive, payment, vendor, item or tax is ever written.
Inbound	Contacts, items, purchase orders, receives, bills	Read by sweeps into an inbox, then adopted: an order with valid dimensions links to the local order; a mismatch raises a coded reconciliation exception.
Control totals	Ours vs theirs per window	Not available in this build (the tenant side has no endpoint); the screen says so with code CONTROL_TOTALS_UNAVAILABLE.

Zoho ERP Connector shows the connection mode (LIVE_WRITE on UAT), token health, the last sweeps and the adoption results. The connection host and organisation are pinned; a write to any other organisation or module is refused before it leaves.

13. Frequently asked questions

I cannot sign in. What should I check?

User id exactly as issued (they are upper case, like U-REQ), the correct password, and whether several failures have throttled you: wait a few minutes. If you still cannot sign in, use Forgot password or ask the Administrator.

Why is there no "Continue with Zoho" button?

The owner has not yet configured the Zoho single sign-on client. The button appears automatically once all its settings exist. WBS sign-in always works.

I asked for a reset link and no e-mail came.

On UAT mail is recorded, not sent. The Administrator can release the link from the notification outbox if the owner has enabled that; otherwise ask the Administrator to set a temporary password through the coordinator.

A screen I need is missing from the menu.

Your role does not hold its permission. The menu only offers what the server will allow; typing the address is corrected back to Home.

My request went to "Exception Pending" instead of "Submitted".

The control cell has less available budget than the value requested. It is routed to a FinanceApprover with the shortfall shown; a reason is required. Alternatively raise a budget revision first.

"SELF_APPROVAL" when I press Approve.

You raised or edited that object. Ask an independent approver. An Administrator may override with a written reason; the override is recorded and notified.

The Approve button is not shown to me on a row.

Approval needs the specific permission for that stage (ProcurementApprover for within-budget, FinanceApprover for exceptions and revisions, CapitalisationApprover for capitalisation), and the object must be in a decidable state.

My export stays at "queued".

Your browser drives the export; keep the page open. If it was closed, open the screen again and press Export again.

Excel export refused: "too large".

The workbook is capped at 20,000 rows. Use CSV, or narrow the entity/plant filters.

Why does the PO screen show Amend/Cancel/Close for some users and not others?

Those are ProcurementApprover (and Administrator) actions; other roles see "not permitted for your role".

Internal material request refused with INTERNAL_MAPPING_MISSING or VALUATION_NOTE_REQUIRED.

The cell has no budget-owning mapping, or a manual valuation was entered without the note that explains its source. Fix the mapping or add the note; the exception is retracted when resolved.

"IMR_ALREADY_LIVE".

A line can carry one live internal request at a time. Cancel or complete the existing one first.

The audit verify says NEVER_ANCHORED. Was the log tampered with?

No. The chain is intact; the daily anchoring schedule is not yet running on UAT. Whole-stream deletion cannot be detected until it is.

Control totals show 503 CONTROL_TOTALS_UNAVAILABLE.

By design: the tenant provides no endpoint for its side of the comparison. Reconciliation still balances line by line.

Will the demo Zoho tenant receive real orders from my testing?

Only an approved order that you explicitly emit is written, to the demo tenant only, once. Nothing else is written to Zoho.

A notification I expected is missing from my history.

Notifications go to users who have an e-mail address on their PostgreSQL profile and hold the receiving role in the object's project scope. Check your preferences, and ask the Administrator to look in the outbox.

Where are figures in "L" and "Cr"?

Lakh (₹1,00,000) and crore (₹1,00,00,000), Indian grouping. Detail tables show full rupees; internally everything is paise.

The page shows "This screen could not be loaded".

A module failed to load, usually a network hiccup. Reload the page; if it persists, report it with the time and screen name.

14. Settings the platform owner controls

These are environment settings of the Catalyst AppSail service, set by the platform owner, never by testers. Names only; no values appear here.

Setting	Effect	Status on 14 September 2026
CAPEX_OIDC_ISSUER , CAPEX_OIDC_AUTH_URL , CAPEX_OIDC_TOKEN_URL , CAPEX_OIDC_JWKS_URL , CAPEX_OIDC_CLIENT_ID , CAPEX_OIDC_CLIENT_SECRET , CAPEX_OIDC_REDIRECT_URI	Enable "Continue with Zoho" (all seven required).	Not set; button hidden.
CAPEX_MAIL_ADAPTER , CAPEX_MAIL_FROM , CAPEX_MAIL_FROM_NAME	Send real mail through Catalyst Mail from a verified sender.	Recording adapter; no mail leaves.
CAPEX_UAT_REVEAL_RESET_LINKS	Let Administrators release reset links from the outbox (audited); ignored once real mail is on.	Not set.
CAPEX_NOTIFICATIONS_DISPATCH_SECONDS	Automatic dispatch interval.	Not set; manual dispatch.
CAPEX_BREAK_GLASS_USER_ID	The one Administrator account exempt from Zoho sign-in, audited on every login.	Not set; owner to choose.
Audit-anchor Cron Function	Signs each day's audit chain.	Not deployed; verify reports NEVER_ANCHORED.

Reference documents in the repository: [docs/fable51/UAT_OWNER_ENABLEMENT_2026-09-14.md](#) (owner steps), [docs/fable51/IDENTITY_AND_NOTIFICATIONS.md](#) (sign-in and notifications design), [docs/fable51/evidence/release/UAT_ACCEPTANCE_2026-09-14.md](#) (acceptance evidence), [docs/runbooks/audit-anchor.md](#).
